



OSU Spears School of Business Building

Oklahoma State University



MAY PROGRESS REPORT

June 1, 2015



MONTHLY OVERVIEW

- Progress Continues on the Morrill Street Utilities.
- Set Morrill Ave Electrical Vault
- Demo of Stacks.
- Advertise Bid Package II.
- Coordination with OSU on Trailer Compound and Sub-contractor Parking Locations
- Tied Into 18" Existing Chill Water Lines
- Moving of Construction Fence to Permanent Location

Monthly Progress Report

As construction continues, Manhattan will issue monthly progress reports throughout the construction process. Typically, these reports are generated and transmitted on the last day of each month. These reports are meant to serve as a tool for OSU Long Range Facilities Planning to document production and keep interested parties updated with progress who may not otherwise be involved on a daily basis.

PROGRESS REPORT: During abnormal amount of rain this month activities continued on the dry days. The demo of the stacks is near completion. The shutdown of the 18" chilled water lines was a success with no interruption of campus events. Coordination continues for the Morrill Street Utilities Project. Activities this month are all in preparation of starting excavation next month.

Manhattan is proud to partner with OSU Long Range Facilities Planning, Spears School of Business, and Elliot and Associates on this project.

ISSUE NO.02



DEMOLITION



Pictured: The progress of the stack demolition





ELECTRICAL VAULT




Pictured: The installation of Morrill Street electrical vault





CHILLED WATER TIE-IN

Pictured Right: Removal of existing chilled water lines

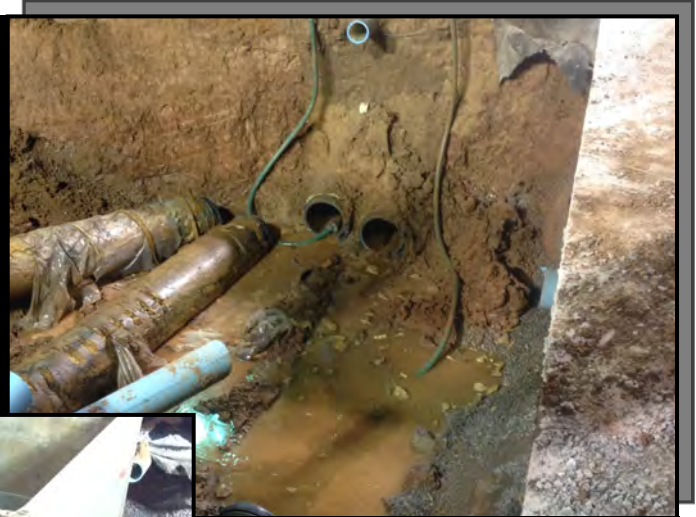

Pictured Left: New pipe and valves to new chilled water lines running east


Pictured Right: Reconnecting water lines above chilled water lines



Pictured Left: Preparing Hester Street to reopen after shutdown



MONTHLY PROGRESS

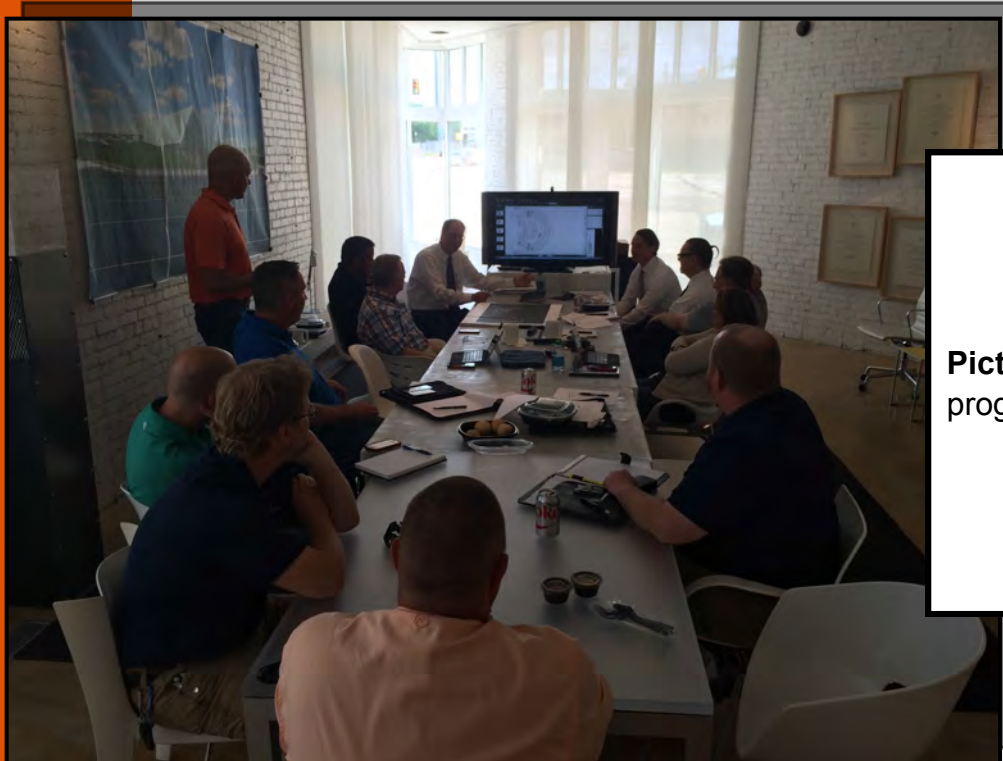

Pictured Left: May progress meeting




Pictured Right: Summer interns hanging mesh screen around construction site



AERIAL PHOTO



May 2015

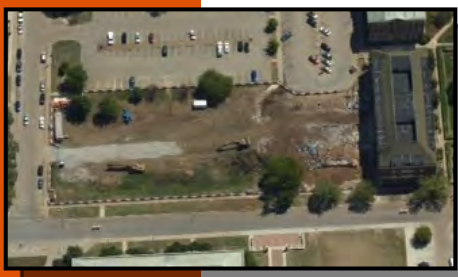


April 2015




May 2015



June 2015



July 2015



August 2015



September 2015



“The only thing better than recognizing a quality product is building one.”

www.manhattanconstruction.com



Manhattan Project Team

Vice President, Oklahoma City

Mark O’Rear

Project Director

Kyle Nelson

Project Manager

Chad Kendrick

Sr. Superintendent

Justin Fegel

Superintendent

Paul McGuire

Assistant Project Manager

Zac McGrath

Assistant Superintendent/

Safety Engineer

Ben Hobson

Estimator

Phil Brandt

Field Accountant

Sharon Muse

Intern

Aaron Kirkpatrick

Intern

Kyle Wanzer

Intern

Joshua Deibert

UPCOMING ACTIVITIES

- Completion of Stack Demo
- Mobilize Excavation & Retention Subcontractors
- Completion of South and East Electrical Duct Bank and Vaults
- Tie-in and Capping of Chilled Water Lines
- Paving of Morrill Ave
- Preconstruction Meetings with Excavation and Retention Subcontractors
- Mobilize Trailer Compound
- Award of Bid Package II

TO SEE A LIVE FEED GO TO

WWW.SPEARS.OKSTATE.EDU/BUILDING/LIVE/

&

WWW.SPEARS.OKSTATE.EDU/BUILDING/LIVE2/

L R F P

Oklahoma State University,
Long Range Facilities Planning,



DETERMAN SCHEIRMAN, INC.
CONSULTING ENGINEERS



TM
